



# Fisherman's Wharf Forward

Update to FWAC

January 7, 2026



SITELAB urban studio

ARCADIS

# Agenda

## 1. Near Term Project Updates


- Smokehouse
- Alioto's Demo, New Plaza
- Other Near Term Efforts

## 2. Long Term Project Schedule and Outreach

## 3. Next Steps

# Fisherman's Wharf Forward



## Near-Term Construction Efforts

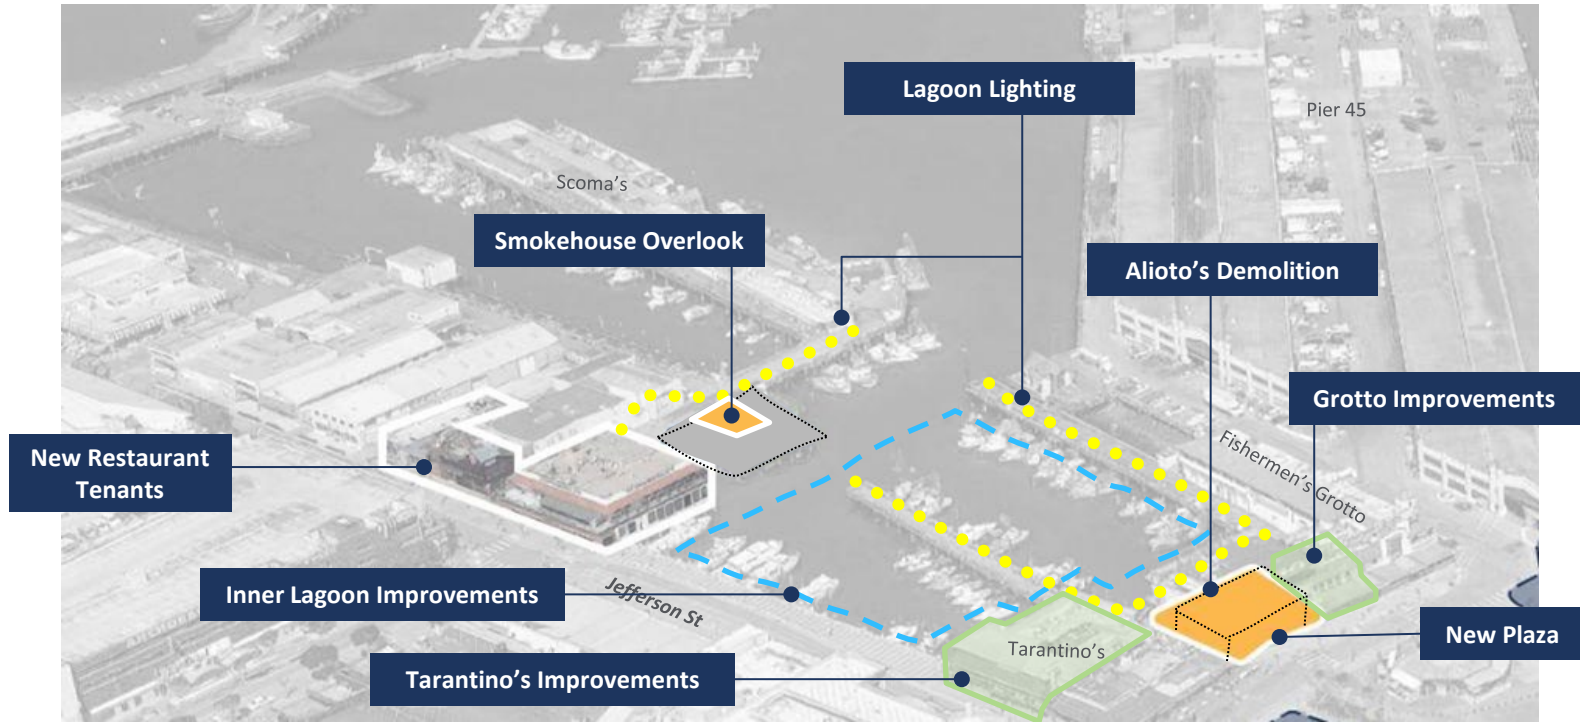

# Schedule Update – Smokehouse Demolition

*\*Target dates, subject to change*

Item	Date
Demo mobilization	10/6/2025
In-water work complete (and removal of barge)	11/25/2025
Start reconstruction of overlook deck	January 2026
Overlook completion	End February 2026*

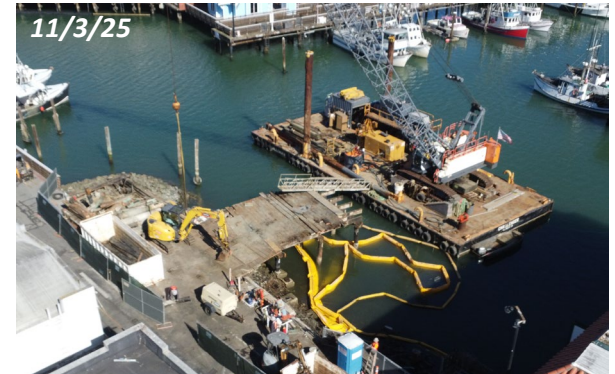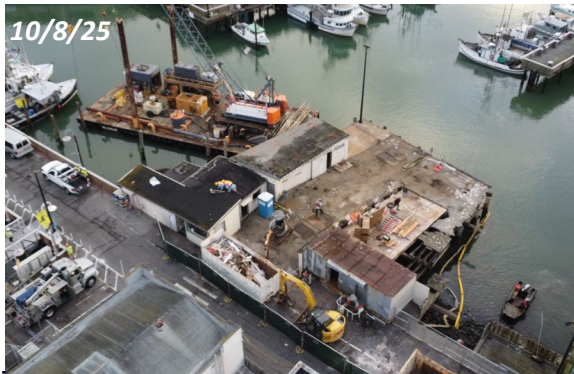

Smokehouse progress, photos by SF Public Works

# Schedule Update – Smokehouse Demolition

*Overlook as of 12/15/2025*



# Schedule Update

## Alioto's Demolition

Item	Date
Tenant notifications on disruption	Started 10/9/2025
Start of hazmat abatement	11/19/2025
Elevator removal	12/12/2025
Fencing extended into sidewalk	12/17/2025
Abatement and safe-off complete	12/30/2025
Removal of signs (with street closure)	1/5-1/6/2026
Structural demolition (with sidewalk closure)	Starting 1/7/2026*
Demolition complete	Mid-February 2026*


*\*Target dates, subject to change*



*Abatement progress*



*Fencing & Signage (12/17)*

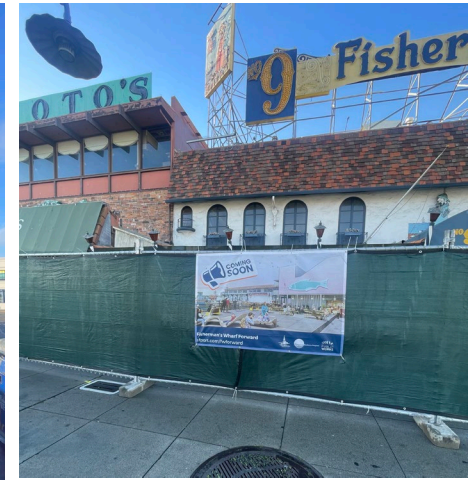

# Schedule Update - Alioto's Demolition



*Sign removal 1/5/2026*

# Schedule Update – Plaza Construction

*\*Target dates, subject to change*

Item	Date
Contract advertised	10/10/2025
Port Commission (Award)	12/9/2025
Start of work	February 2026*
Target Completion	Summer 2026*



*Ground surface update*


## Other Near-Term Efforts

- Lighting
- Plaza - Interactive Railing
- Signage Refresh – Harbor Walk





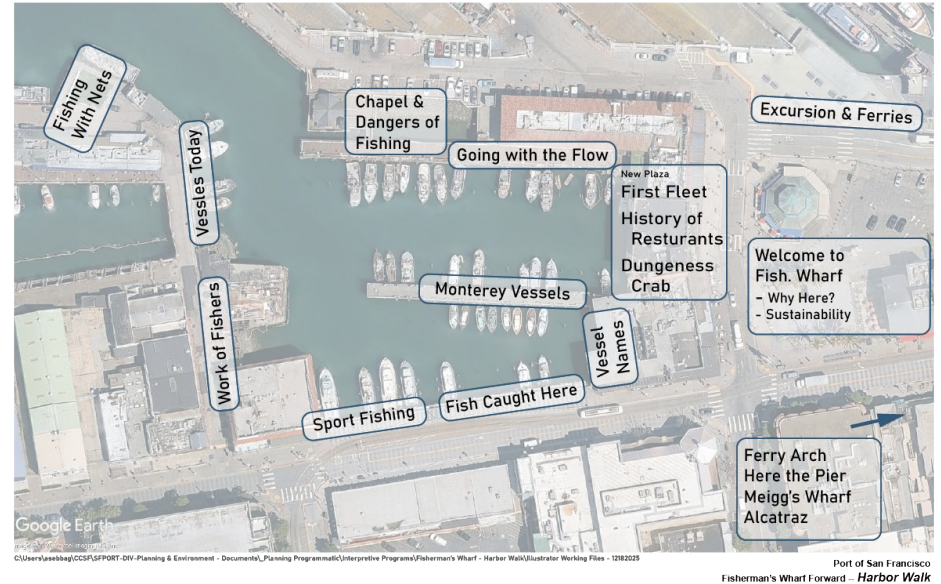


# Signage Refresh – Harbor Walk


Item	Date
Kick-off – In-person Advisory Group meeting	11/17/2025
Story Concepts and Locations	January – February 2026*
Design Development: Ideas & Research	Through March 2026*
Final Design: Prepare for Fabrication	Spring - Summer 2026*
Target Completion	Summer 2026*
Community Engagement	Throughout 2026



*\*Target dates, subject to change*

# Long Term Project

-  Assess Feasibility for Adaptive Reuse of Historic Booth Building & Grotto Facilities
-  Historic Booth Building
-  Seismic and Flood Resilient Improvements, Enhanced Plaza + Public Realm including interpretation of history of the Wharf
-  Seismic and Flood Resilient Improvements to support continued Taylor Street Commercial Hub
-  New Reconfigured Harbor to Support and Enhance Fishers

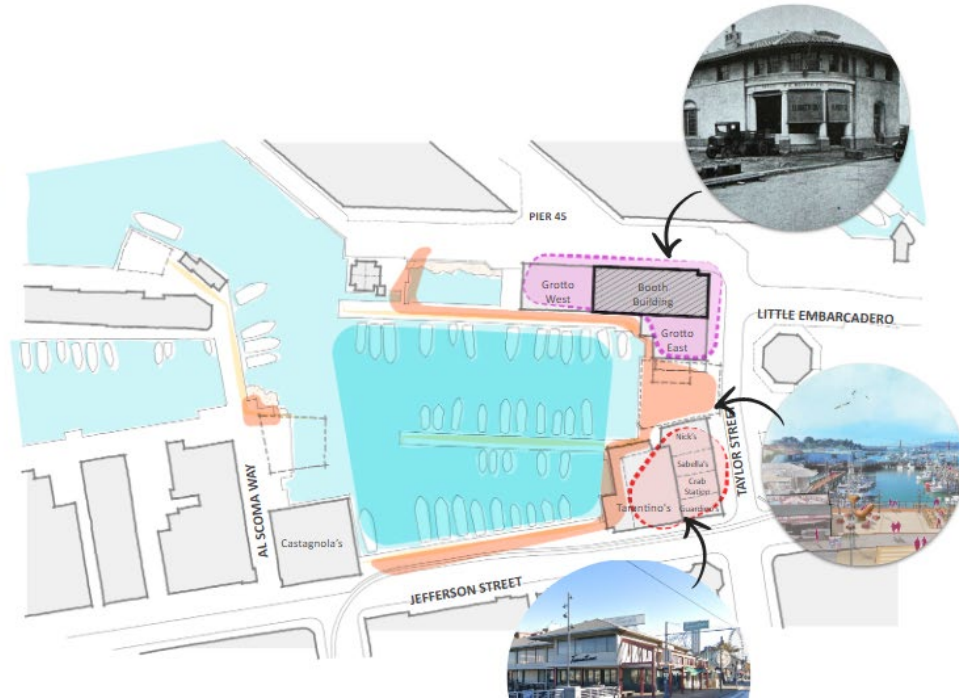

## Schedule (target, subject to change):



# Long-Term Project – Ways to Be Involved

1. Sign up for **FWAC mailings and notifications** on the FWAC website
2. Attend our bi-monthly **FWAC meetings** for updates
3. Visit the **Fisherman’s Wharf Forward website**: [www.sfport.com/fwforward](http://www.sfport.com/fwforward)
4. Visit us at various **local neighborhood events**, FWCBD events, or street pop-ups during the Spring 2026
5. Attend our **Town Hall charettes** and outreach meetings during Summer/Fall 2026
6. Contact us with any questions: [ming.yeung@sfport.com](mailto:ming.yeung@sfport.com), [christopher.horiuchi@sfport.com](mailto:christopher.horiuchi@sfport.com)



Thank you
