



Fisherman's Wharf Forward

Update to FWAC

May 6, 2026




SITELAB urban studio

ARCADIS

Fisherman's Wharf Forward


Near-Term Construction Efforts

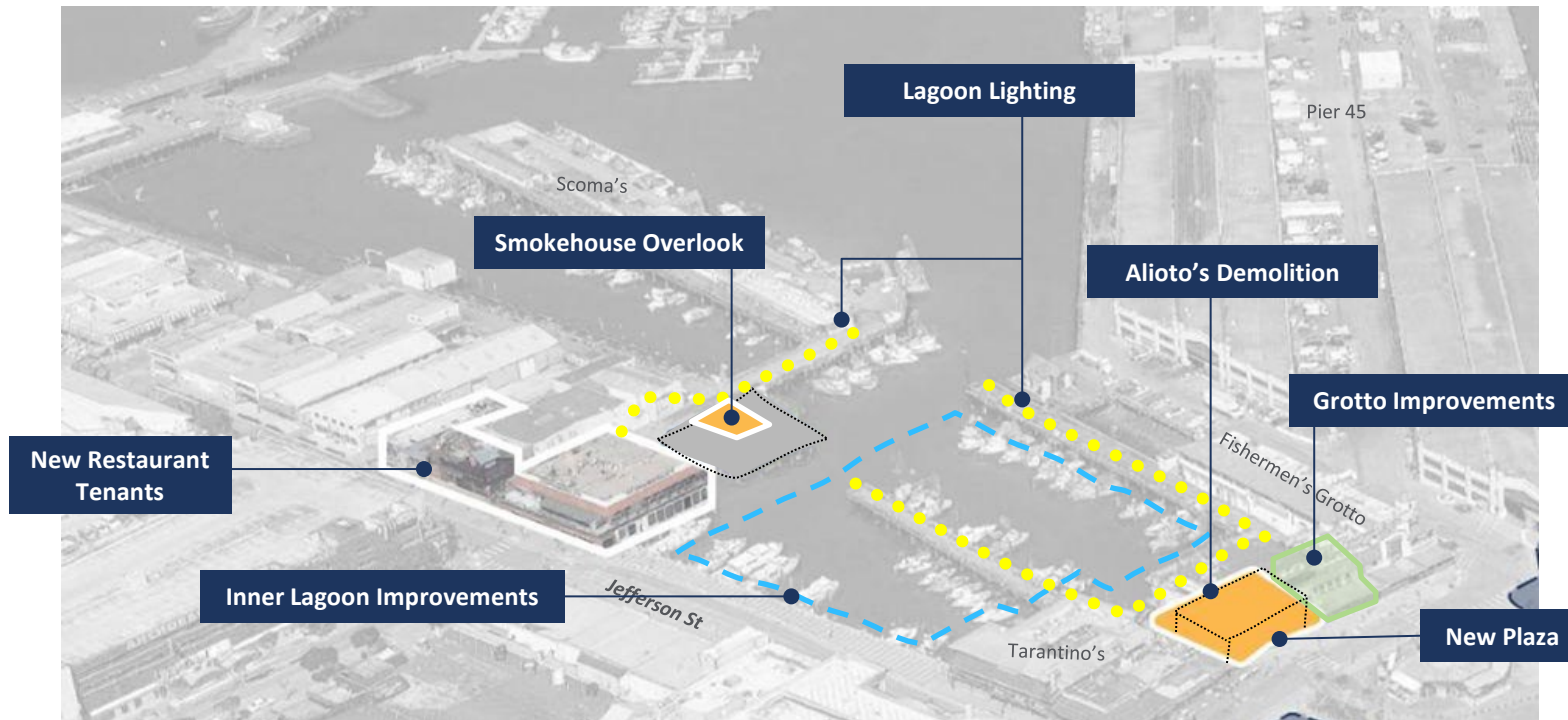

Schedule Update – Smokehouse Demolition

**Target dates, subject to change*

Item	Date
Fuel tank testing and closure	March – April 2026
Crab Hall Lead Abatement	Completed 5/4/2026
Overlook opening	5/22/2026*
Project completion	June 2026*

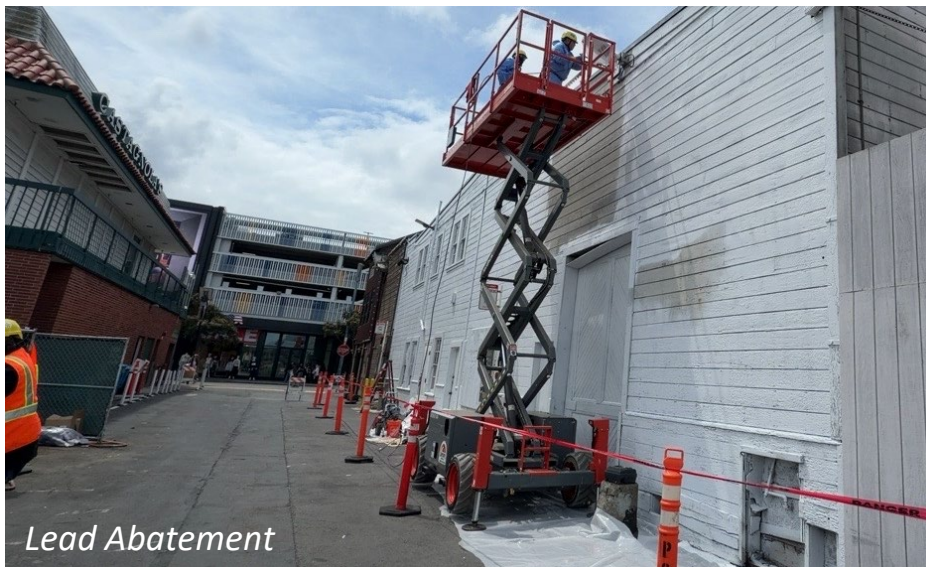

Schedule Update – Plaza Construction


**Target dates, subject to change*

Item	Date
Contract advertised	10/10/2025
Port Commission (Award)	12/9/2025
Start of work (Grotto interior)	Week of 3/2/2026
Start of work (underdeck pile repair)	Week of 3/16/2026*
Target Completion	Summer 2026*




Fisherman's Wharf Forward

Next Improvements (2026 – 2030+)

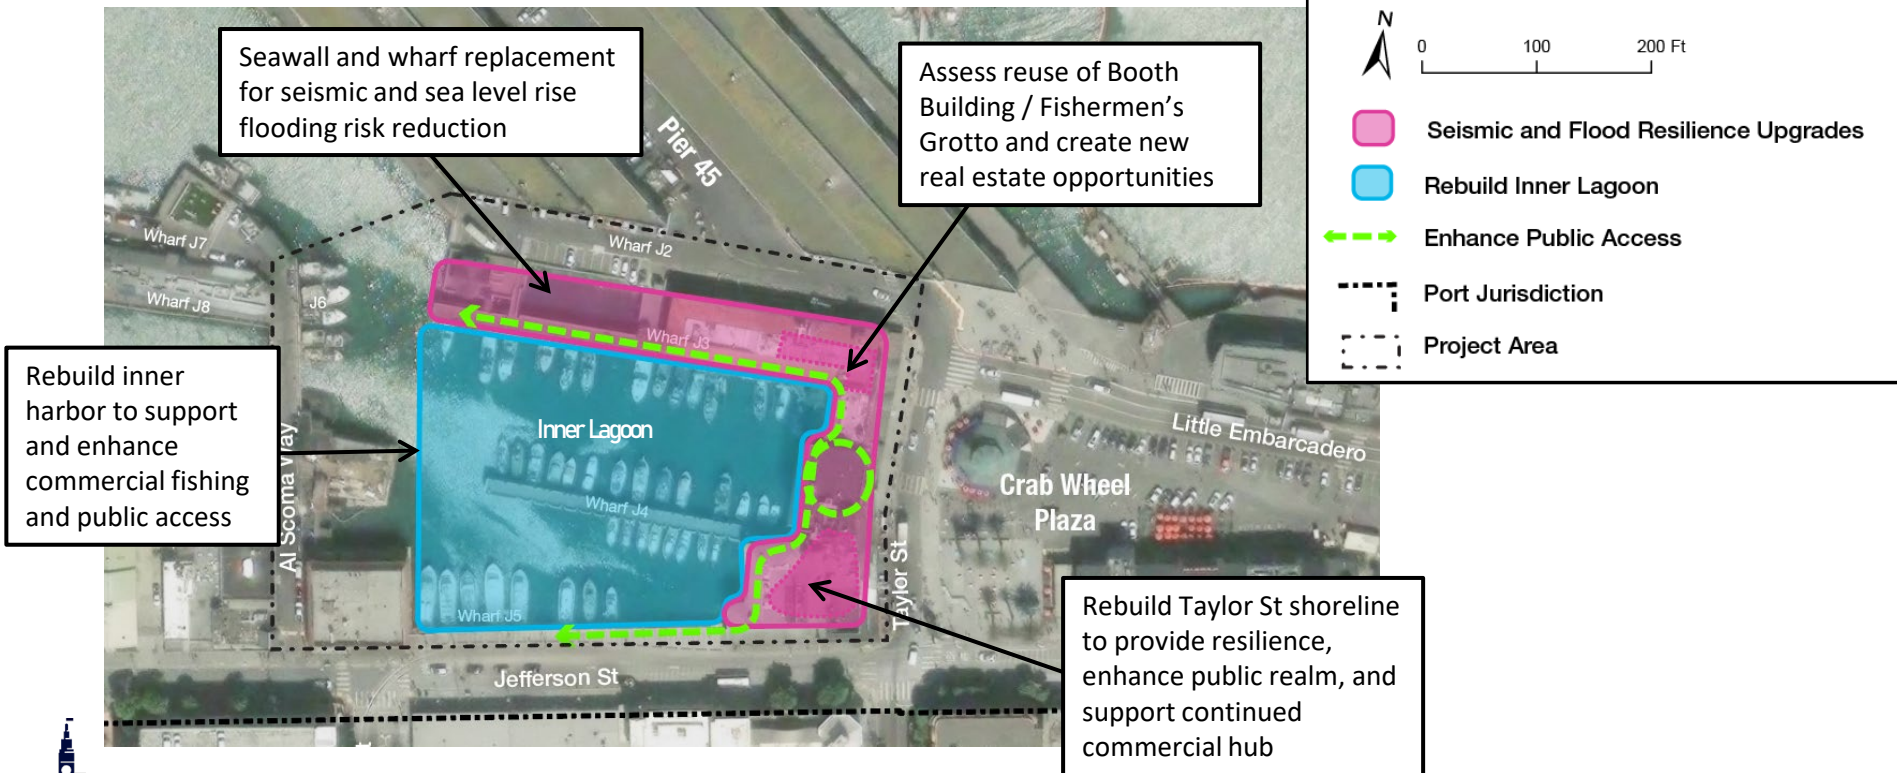

Fisherman's Wharf Forward

Long-term Timeline

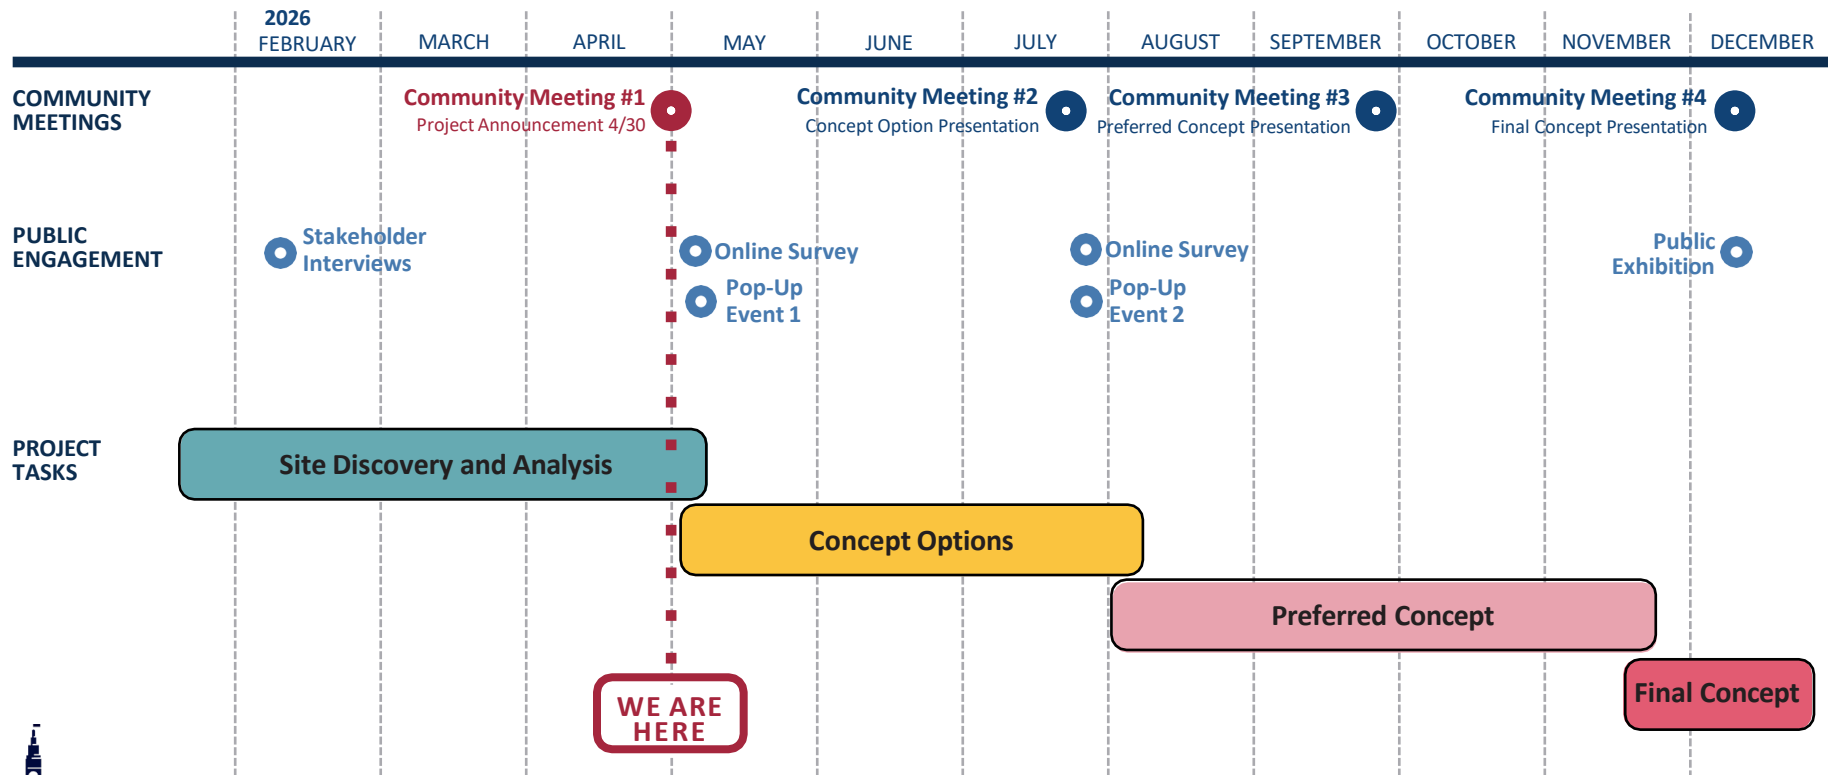

How to engage


Communication and Feedback

Website

- <https://www.sfport.com/fwforward>
 - Near-Term Enhancements
 - Long-Term Resilience Improvements

Email

- fwf@sfport.com
 - Send us your thoughts and questions!

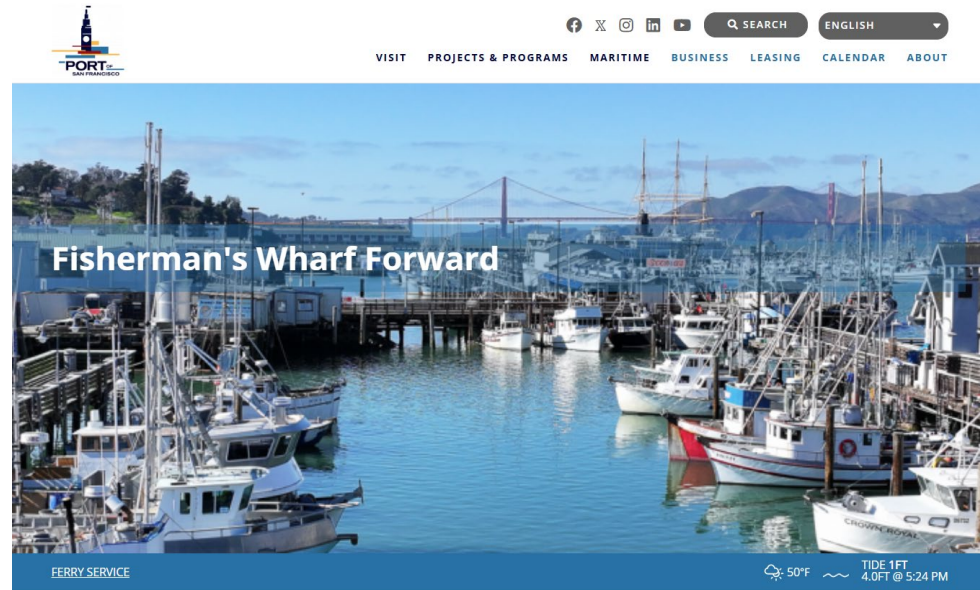

Home

Fisherman's Wharf Forward

Project type: Infrastructure Open Space

How to engage

Online Survey



TAKE THE ONLINE
SURVEY HERE!

An aerial photograph of the San Francisco Fishermen's Wharf area, featuring the Alioto's building and the Fishermen's Grotto. The image is overlaid with a semi-transparent blue rectangle on the left side, which contains the text "Thank you".

Thank you
